




PGCPS . **ENGAGE . DESIGN . BUILD . COMMUNICATE** . PGCPS



BRENT ELEMENTARY SCHOOL

PROJECT PLANNING COMMITTEE MEETING #3 | FEBRUARY 12, 2025





Agenda


- Design Recap
- Construction Updates
- Open Discussion
- Contact

Design Recap

- No design changes since last meeting.
- The design team and PGCPS is coordinating on the site design changes previously discussed.
- Building permitting process has begun.
- Demolition / Site Work has begun (more info in later slides).
- Interior design (Furniture, Finishes and Equipment) is ongoing. Coordination with school needed.
- Pricing for taller guardrails is in progress.

Updated Site Plan

- Pedestrian access to be updated.

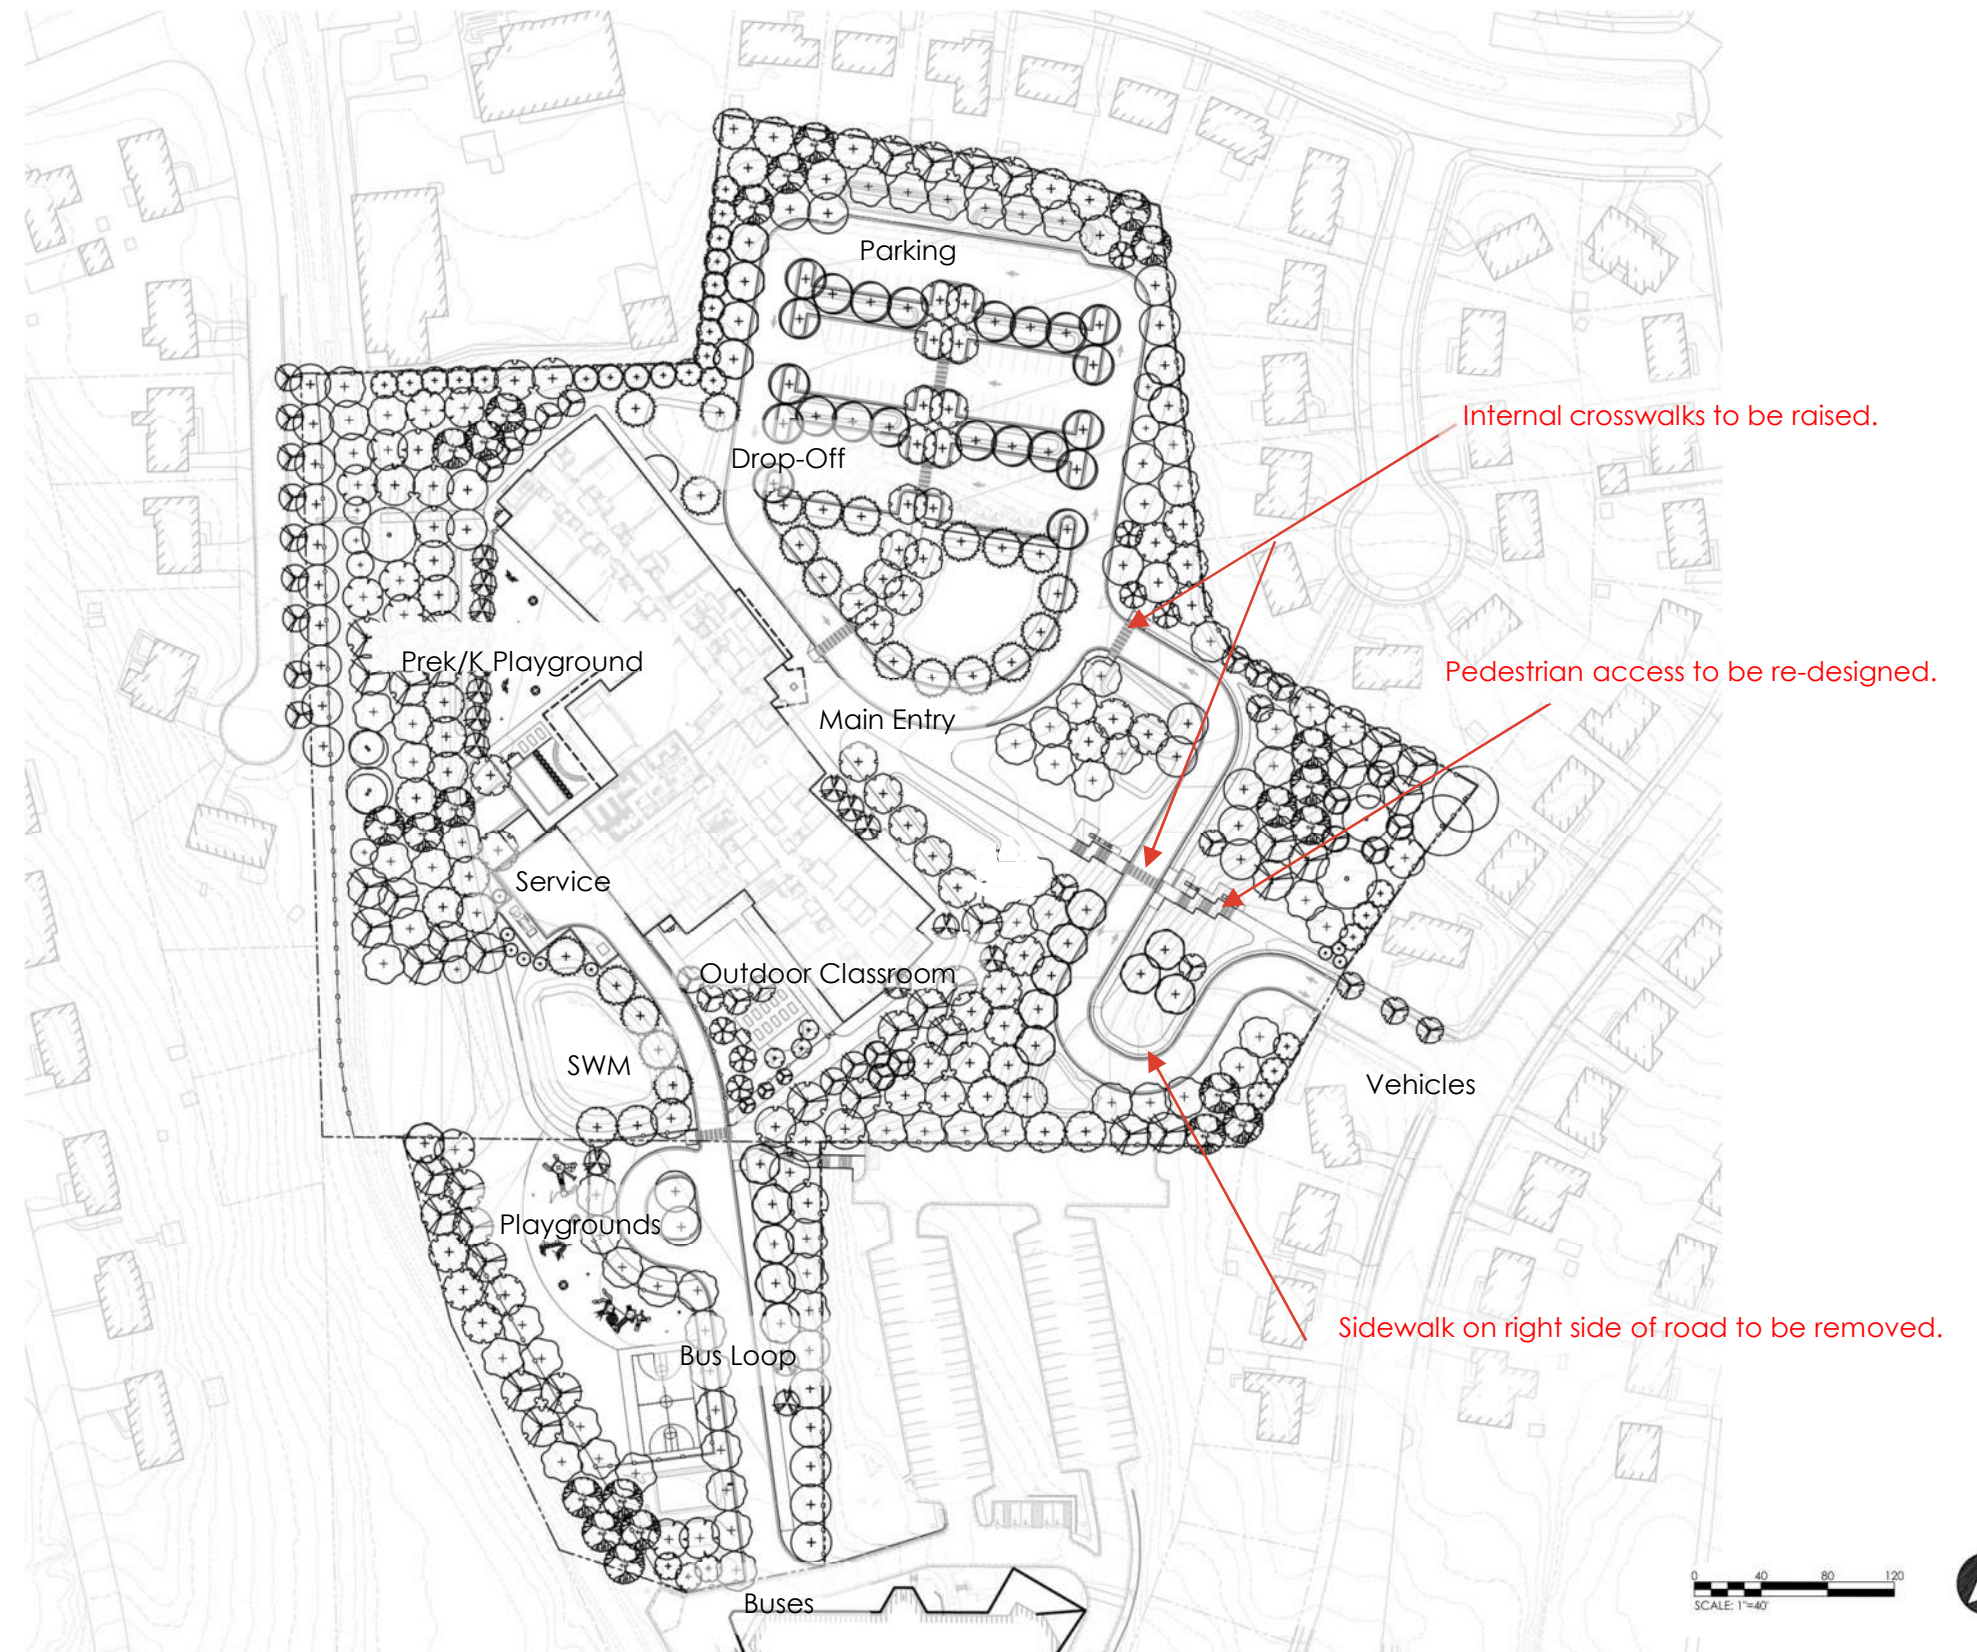

Note: Design is subject to change

Elevations and Renderings





No change from last meeting.




Note: Design is subject to change

School Identity

School to provide more information on:

- School color(s)
- School mascot
- School themes

Schedule Overview

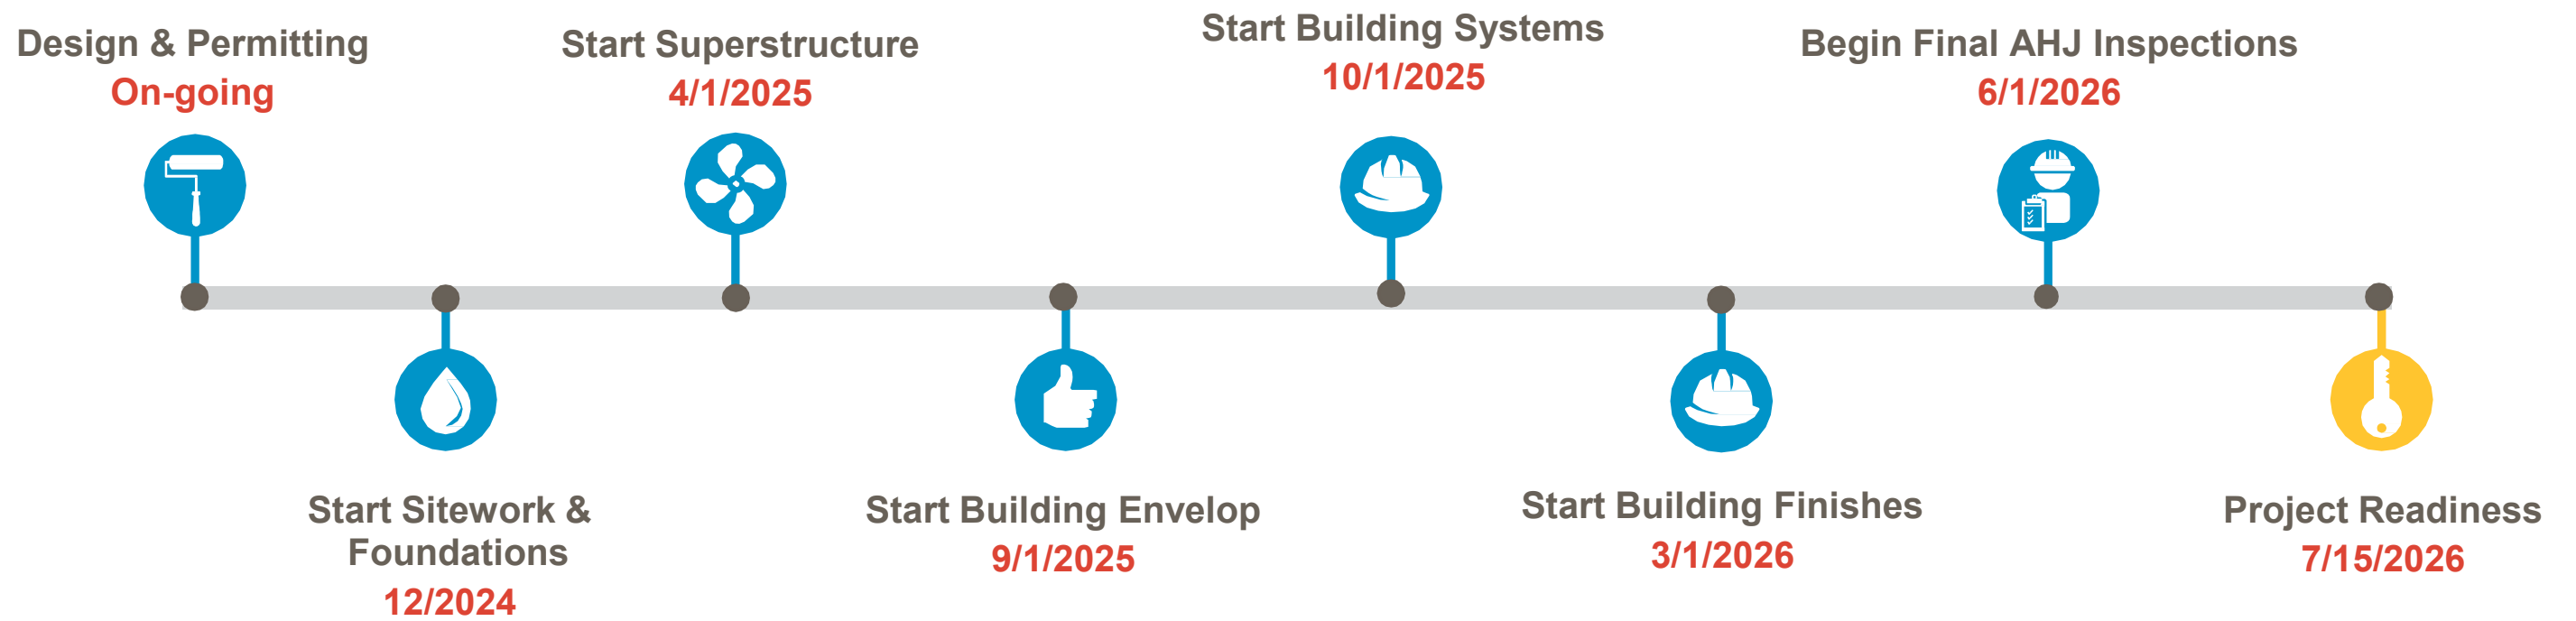


Activities Completed and In progress

- E&S controls set up
- Set up perimeter controls
- Excavation and hauling
- Drilling Geothermal Wells
- Geo-pier Installation

Progress pictures

- Excavation and hauling

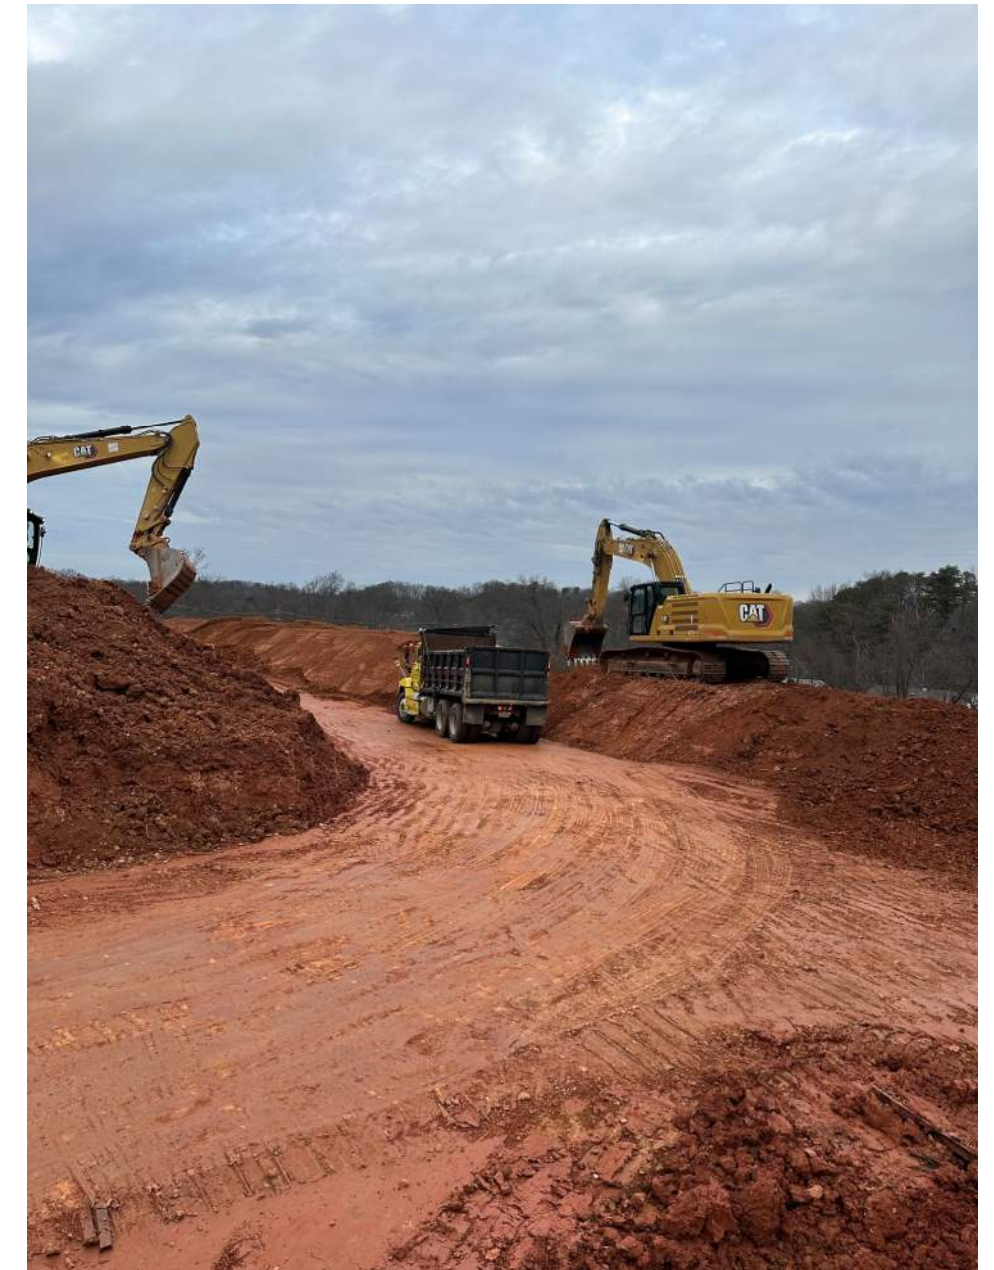

Progress pictures

- Geothermal Installation



- Geo-pier Installation



Upcoming Activities (next 6 weeks)

- Earthwork – Undercut for building pad, continue site excavation
- Geothermal – Complete drilling and horizontal pipes
- Site Utilities – Start installing utility structures
- Concrete – Start footing excavation
- Construction Trailer set-up

Open Discussion

For more information, please contact:



Jam Kendrick

pg_jam.kendrick@pgcps.org

pepblueprintschoolsp3.com

