




PGCPS . **ENGAGE . DESIGN . BUILD . COMMUNICATE** . PGCPS



MARGARET BRENT ELEMENTARY SCHOOL


TOWN HALL MEETING #3 | FEBRUARY 17, 2026



SERVICIOS DE INTERPRETACIÓN


INTERPRETING SERVICES

La interpretación simultánea
está disponible en español.
*Simultaneous interpretation is
available in Spanish.*



SERVICIOS DE INTERPRETACIÓN

INTERPRETING SERVICES



On a computer-- At the bottom of the screen will be an interpretation globe. Click that globe and then select *Spanish*.

En una computadora-- En la parte baja de la pantalla habrá un globo de interpretación. Haga clic en ese globo y seleccione "Spanish."




On a mobile device-- At the bottom of the screen, tap the ellipses icon on the bottom right (...).

- Tap *Language Interpretation*.
- Tap *Spanish*.


En un dispositivo móvil-- En la parte baja de la pantalla, toca el icono de elipses en la parte baja derecha (...).

- Toque *Language Interpretation*.
- Toque *Spanish*.



We value your input.

- Please type your questions/comments in the Q&A area of Zoom.
- Questions and answers from this town hall will be posted on pgcpsblueprintschools.com.



Our Commitment

PGCPS is committed to moving swiftly to deliver safe, state-of-the-art, and sustainable learning environments for our students, teachers, and communities.



Agenda

- Welcome
- Design Recap
- Construction Updates
- Open Discussion
- Contact

Welcome

PGCPS, Department of Alternative Infrastructure, Planning, and Development

- **Shawn Matlock**, *Director*



Welcome

Prince George's County Council

- **The Honorable Eric C. Olson**, District 3



Design Recap

- No major design changes since last meeting.
- Construction continues and we are on schedule.
- Furniture coordination with school has been completed.
- Interior design to be presented today.

Site Plan

- LEGEND**
- ① Entry Plaza
 - ② Parking Lot
 - ③ Bus Loop
 - ④ Drop-Off
 - ⑤ Library Parking Access
 - ⑥ Entry Sidewalk
 - ⑦ Outdoor Classroom
 - ⑧ Bioretention Overlook
 - ⑨ Garden Plots
 - ⑩ Pre-K/K Playground
 - ⑪ Primary Playground
 - ⑫ Paved Play
 - ⑬ Free Play Area
 - ⑭ Monument Sign
 - ⑮ Service Area
 - ⑯ Existing Canal
 - ⑰ Existing Service Access Route
 - ⑱ New Carrollton Public Works
 - ⑲ New Carrollton Branch Library and Parking Lot (PGCMLS)



Note: Design is subject to change

Rendering vs Reality



Interior Design

- Heart of the School
- Main entrance
- Monumental stair
- Library


Image shows Brent but Fairwood is similar.



Interior Design

- Library entrance

Image shows Brent but Fairwood is similar.

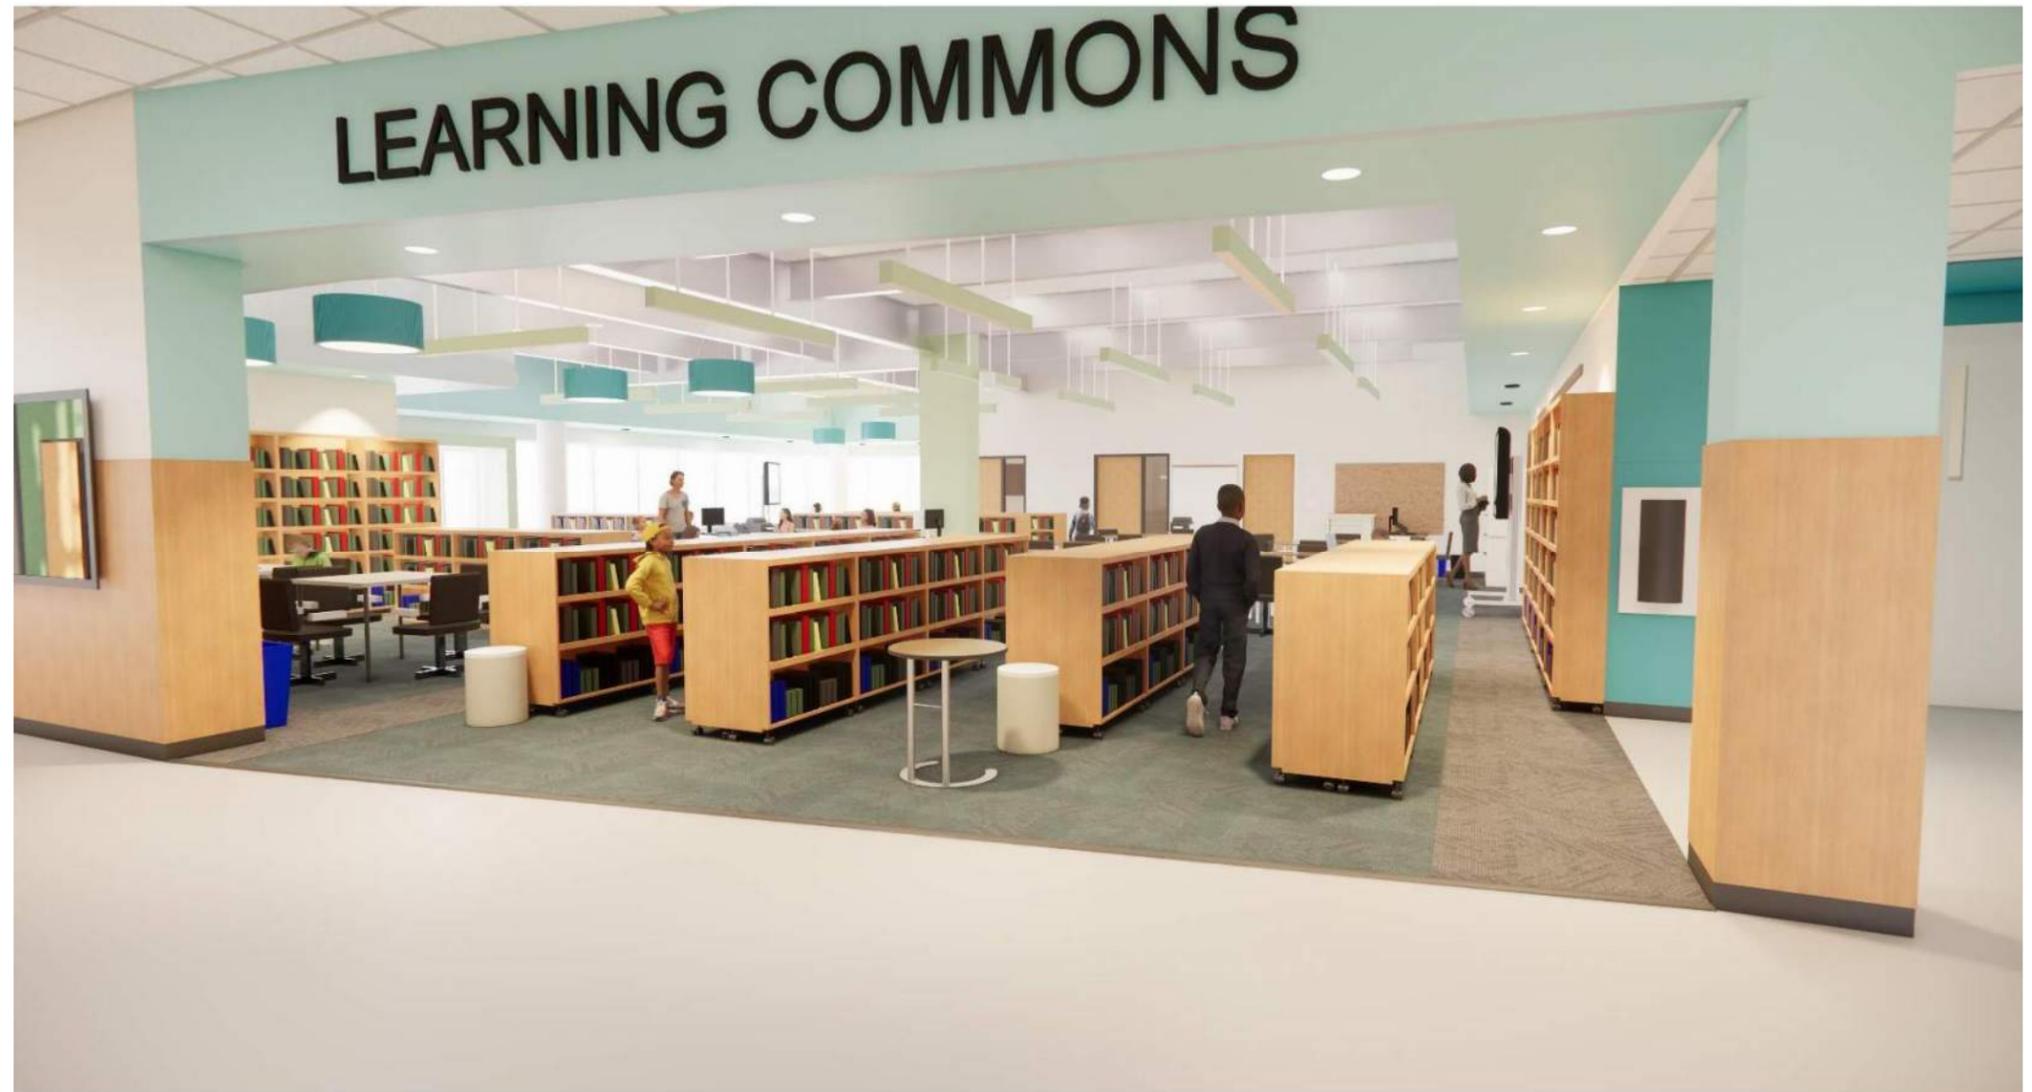

Interior Design

- Dining/Performance space

Image shows Brent but Fairwood is similar.



Interior Design

- Gymnasium

Image shows Brent but Fairwood is similar.




Interior Design

- Collaboration Spaces

Image shows Brent but Fairwood is similar.



Schedule Overview

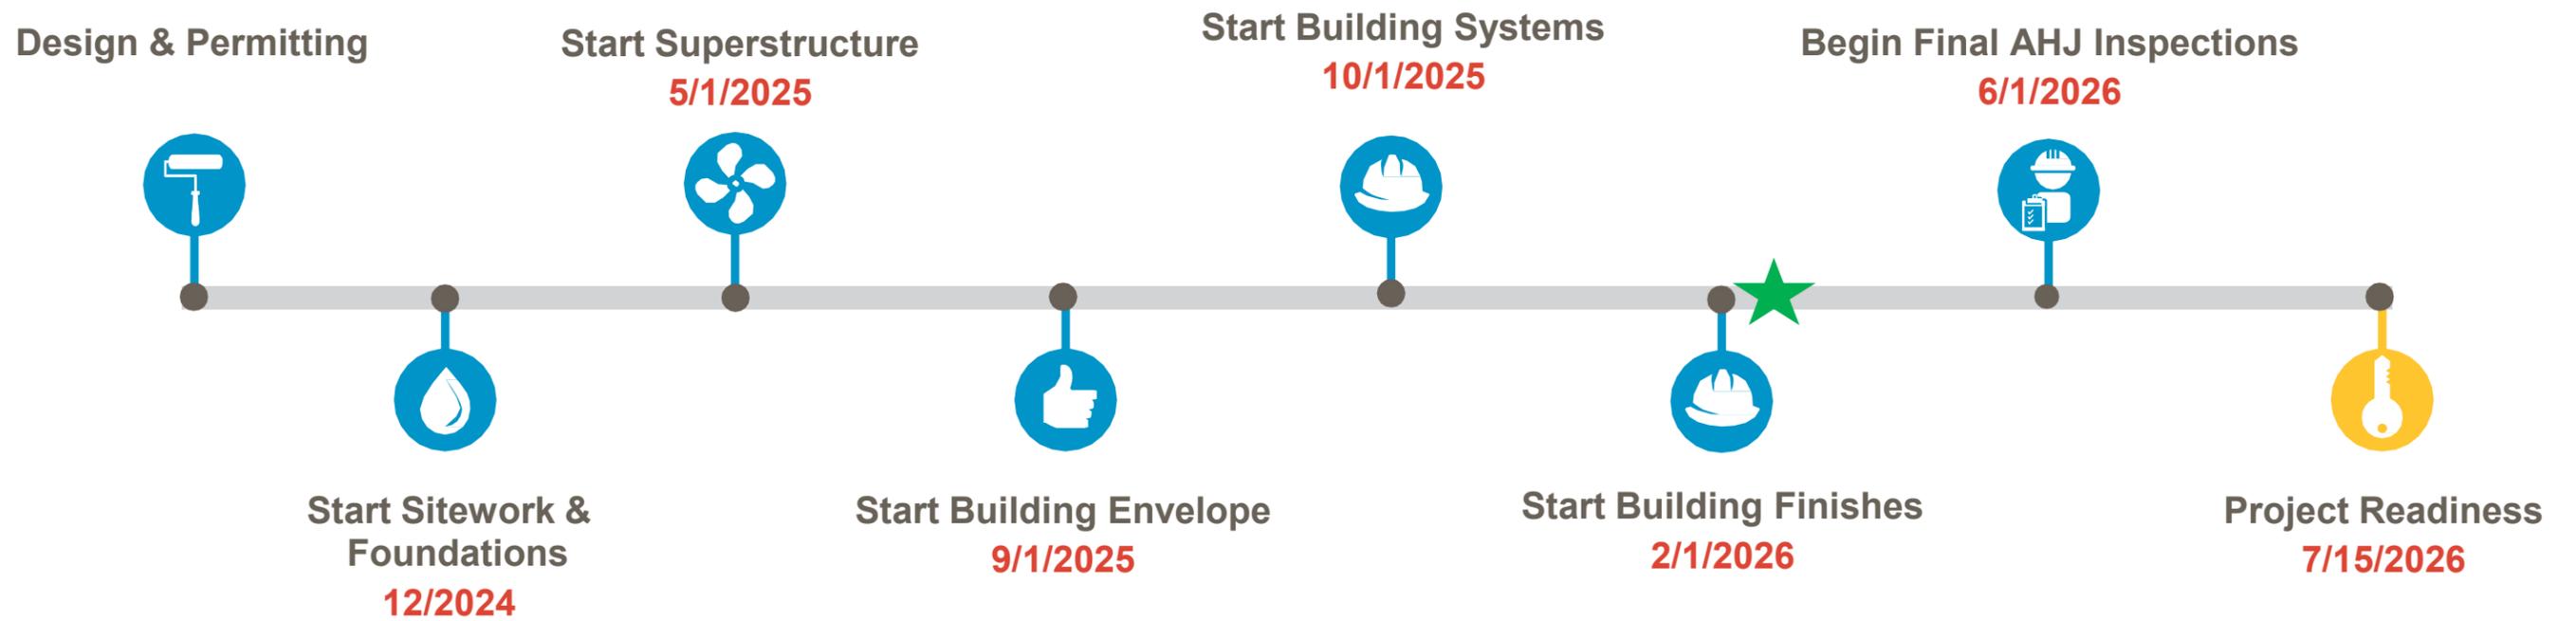

★ **Current Project Completion is about 70 %**

Major Activities Completed and in Progress

- Building Foundation and Superstructure completed.
- Geothermal wells and laterals installation completed.
- Building envelope and roofing installation completed.
- Exterior Façade – About 80% Brick installation completed. Framing for metal panel in progress.
- Windows and glazing – Storefront installation completed. Curtainwall installation in progress.
- MEP in-wall and overhead rough-in installations completed. Equipment installation and connections in progress.
- Drywall – About 90% interior framing and drywall installation completed.
- Ceiling grid, registers and grills, light fixtures and fire alarm devices installation in progress.
- Paint - Priming and 1st coat paint on walls in progress.
- Site work – Site roads, curb and gutter installations in progress.
- Utilities – Permanent power energized, Water and Sanitary lines tied-in to mains, gas line installation completed, telecommunication conduit installation completed.

Upcoming Activities (next 6 weeks)

- Complete brick installation.
- Metal Panel
- Exterior and Interior curtain wall
- Continue ceiling grid installation
- Continue paint
- Flooring and ceramic wall
- Installation of plumbing fixtures
- Millwork
- Mechanical equipment start-up
- Grading and storm structure installation on parking lot area
- Concrete sidewalk and asphalt

Progress pictures

- Aerial View



Progress pictures

- Front of building progress



Progress pictures

- Rear of building progress




Progress pictures

- Brick and Windows





Progress pictures

- Exterior Façade Progress

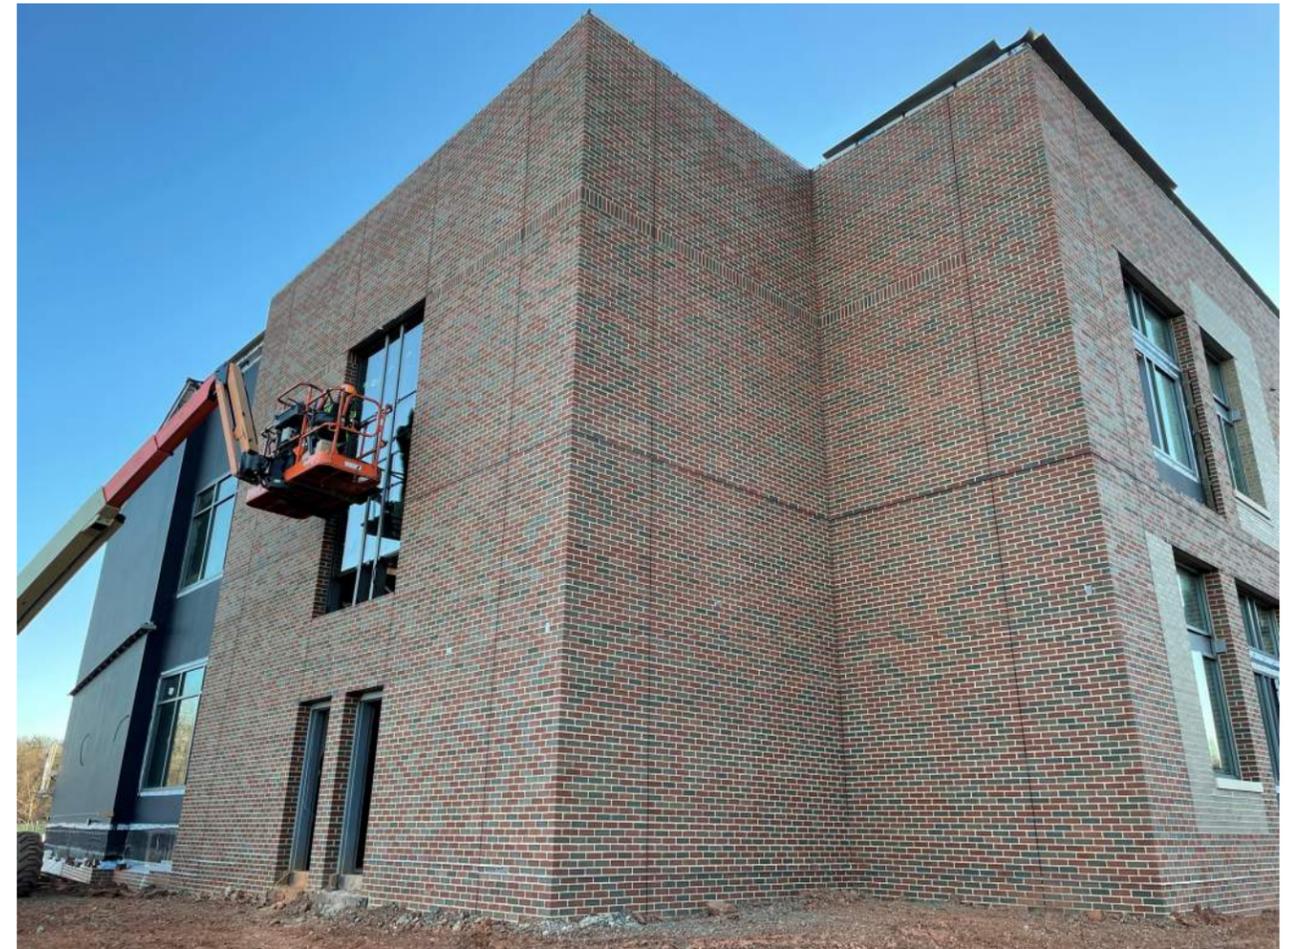


Progress pictures

- Gym

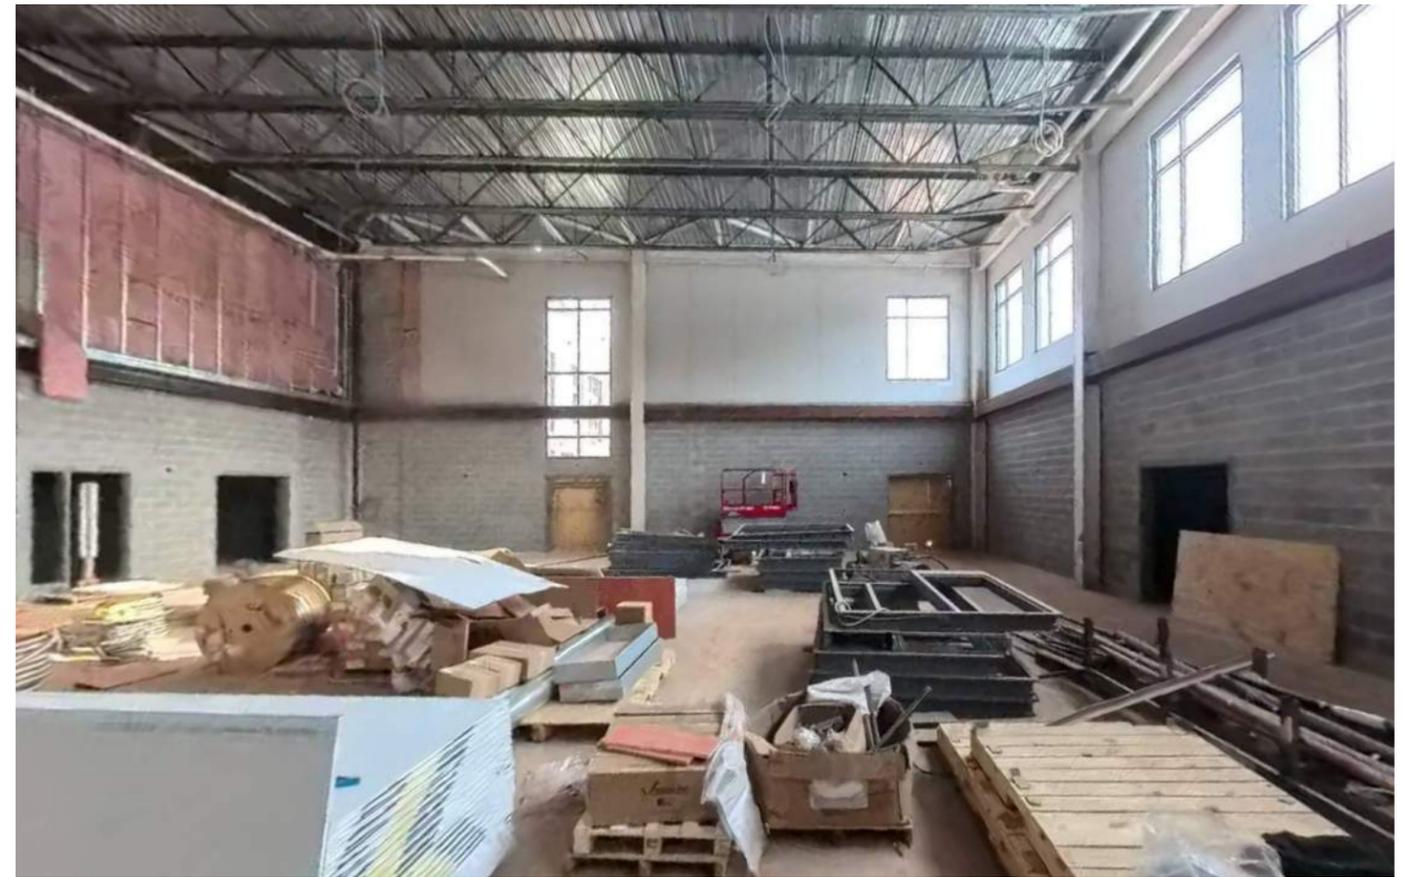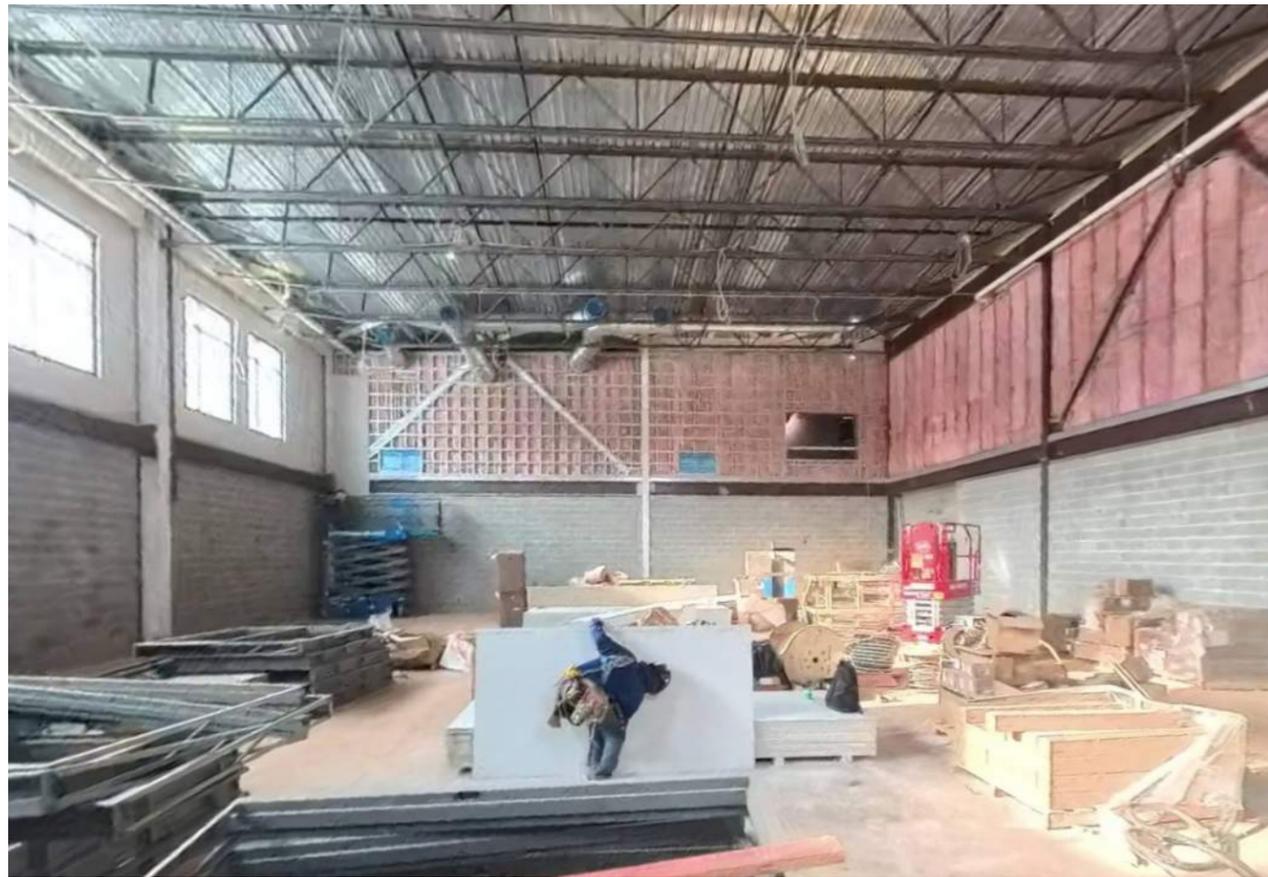


Progress pictures

- Cafeteria

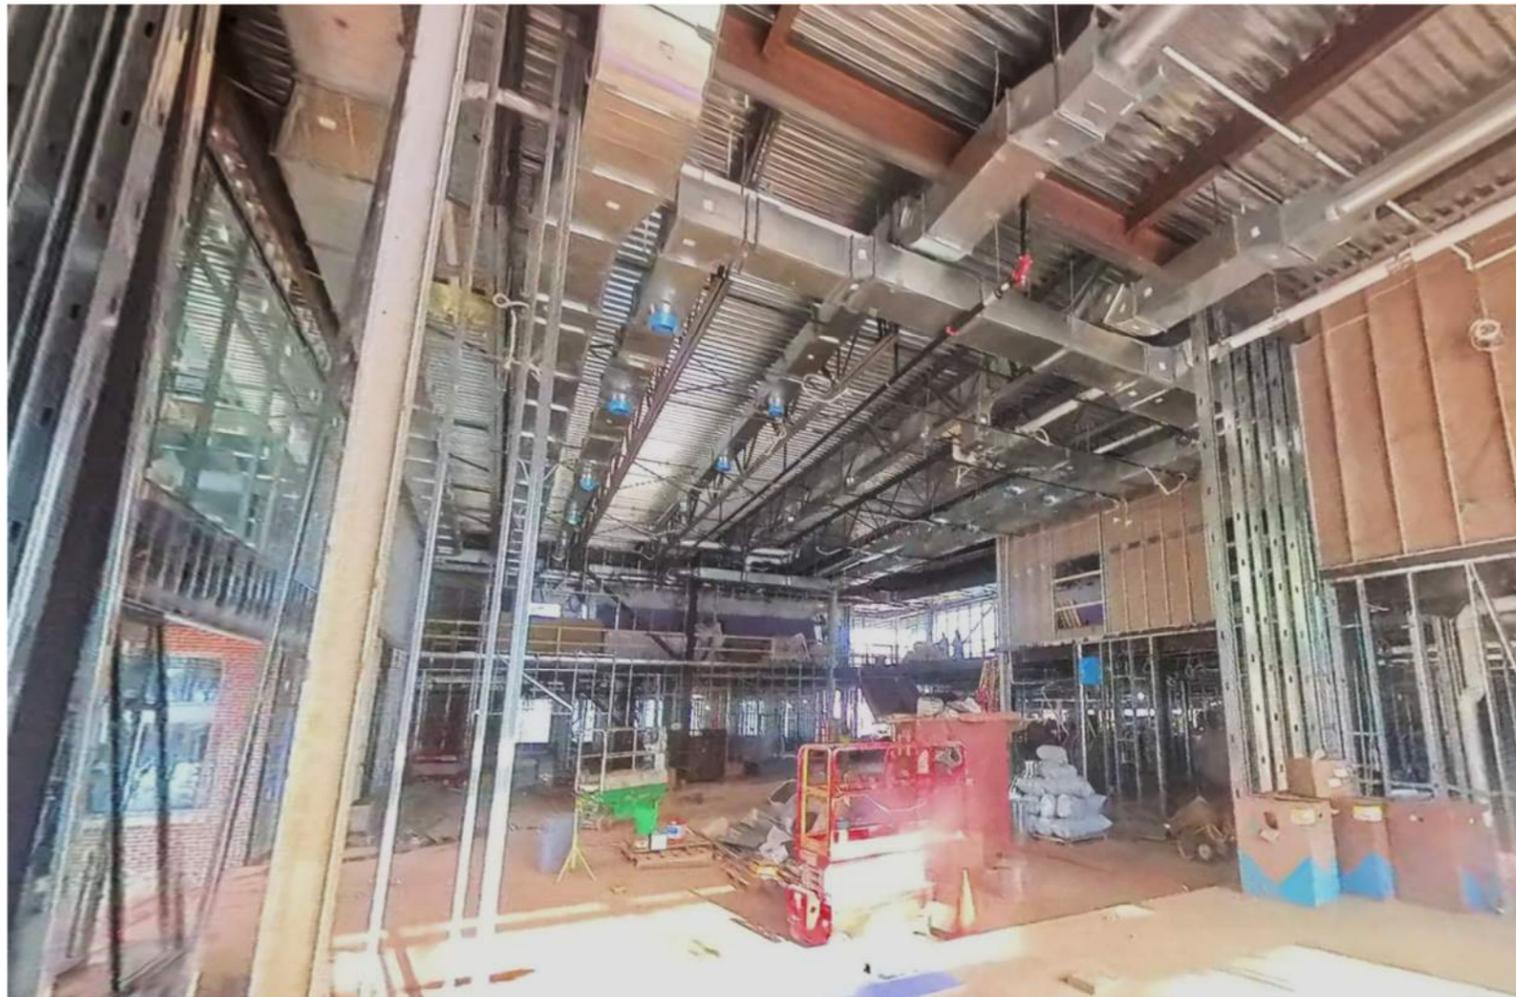


Progress pictures

- Ceiling grids, Paint, Light Fixtures

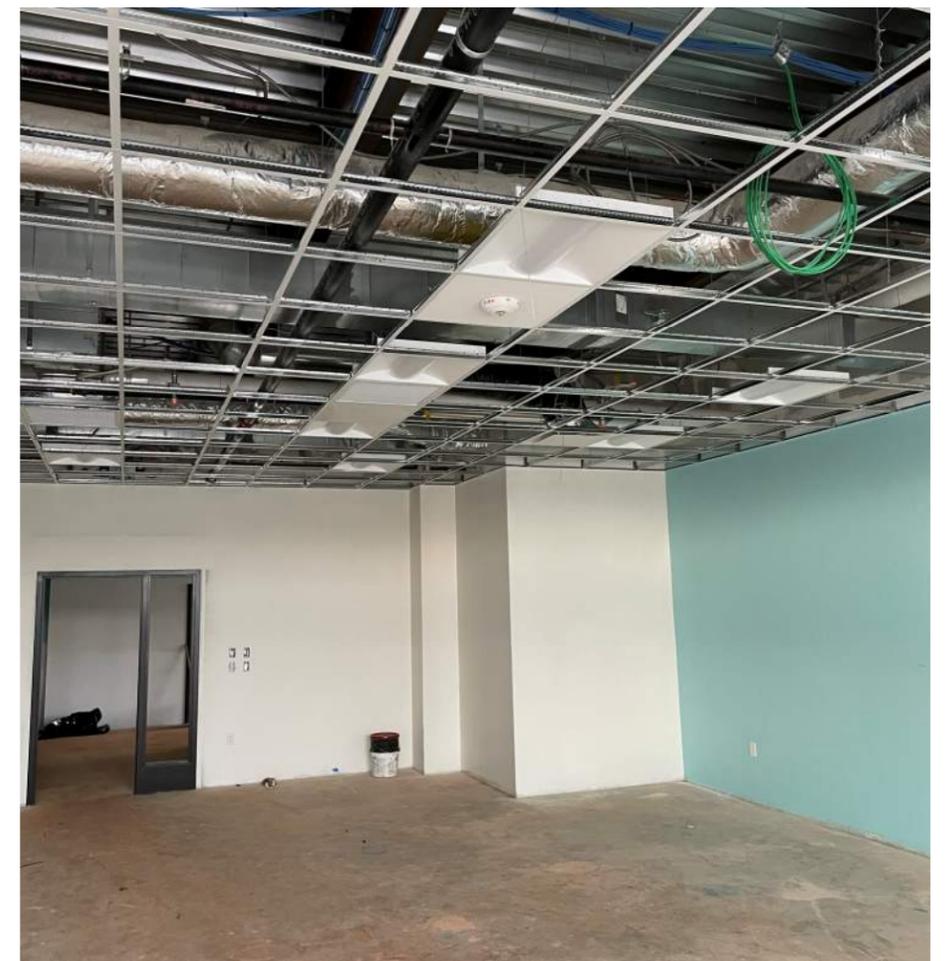

Progress pictures

- Ceiling grids, Paint, Light Fixtures

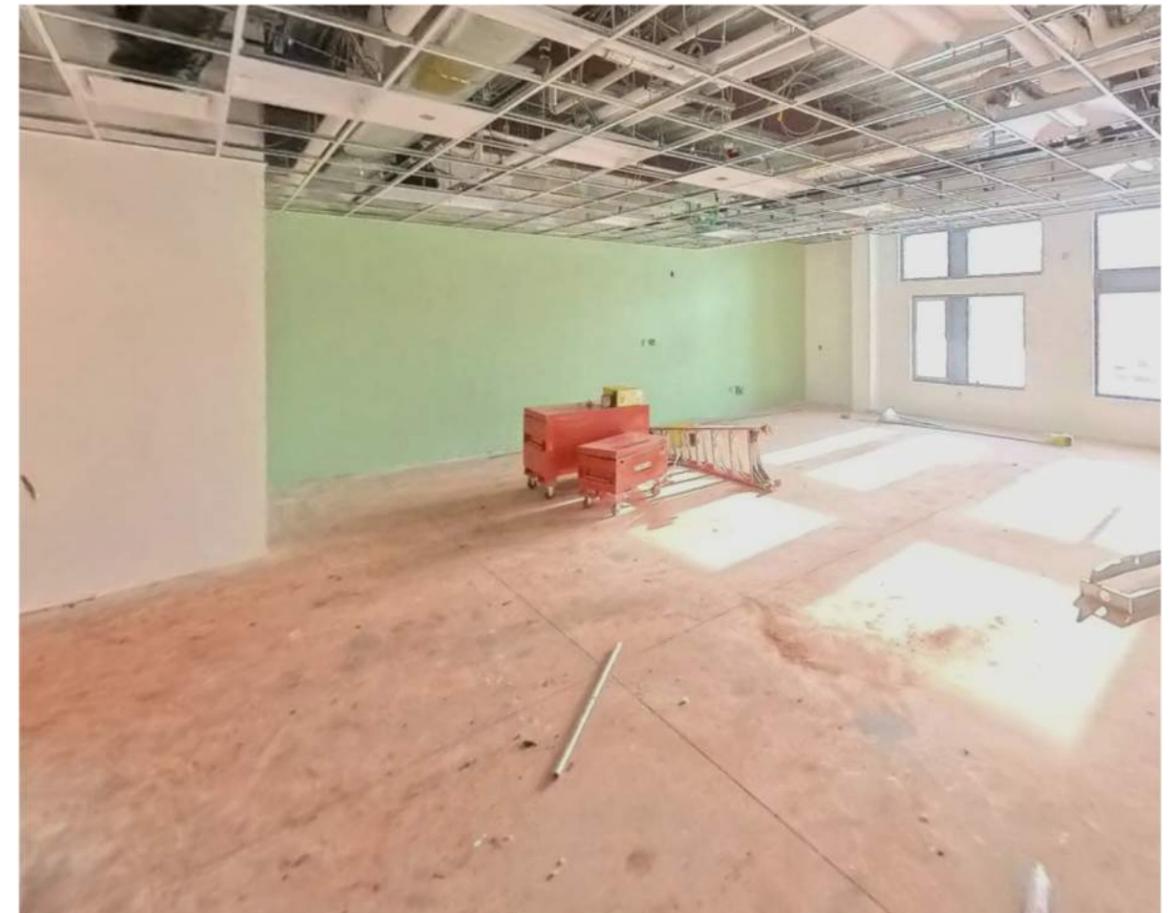



Progress pictures

- Heat Pump/Mechanical Rooms



Progress pictures

- Main Mechanical Room

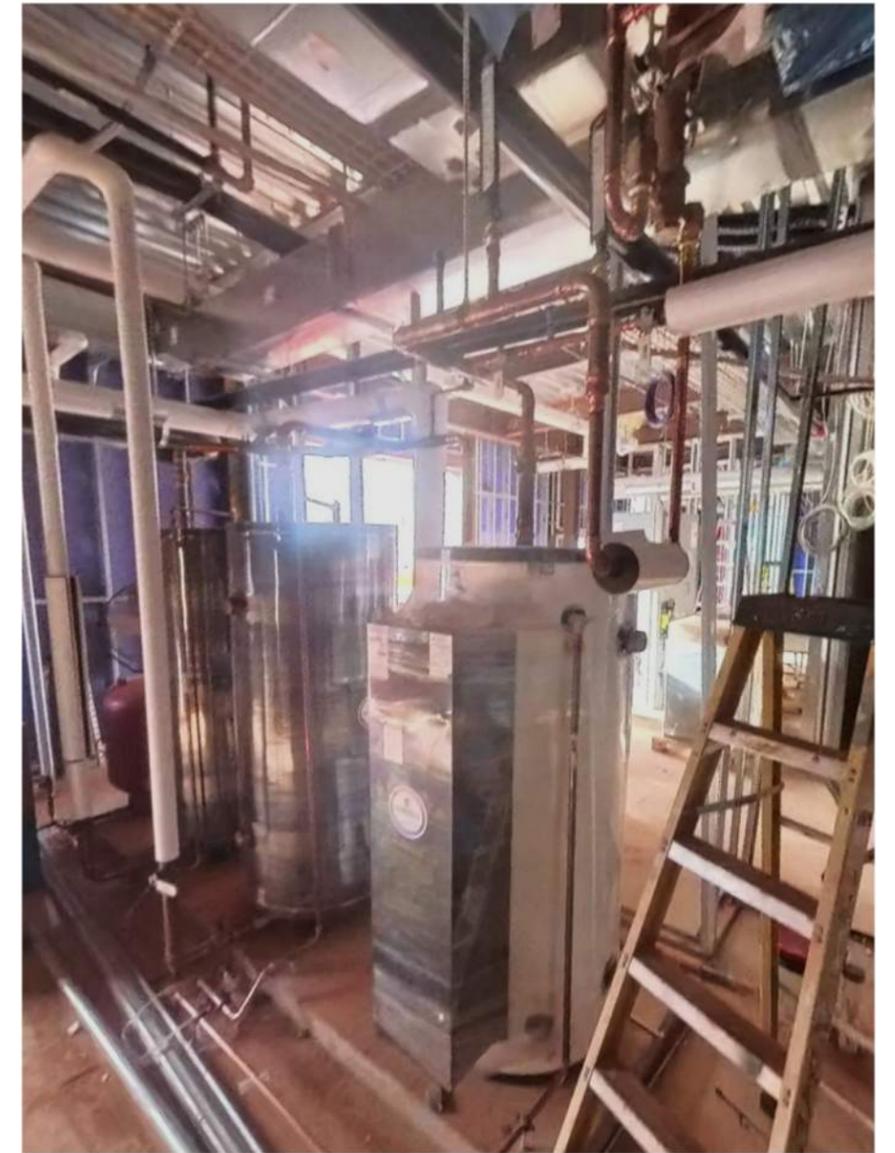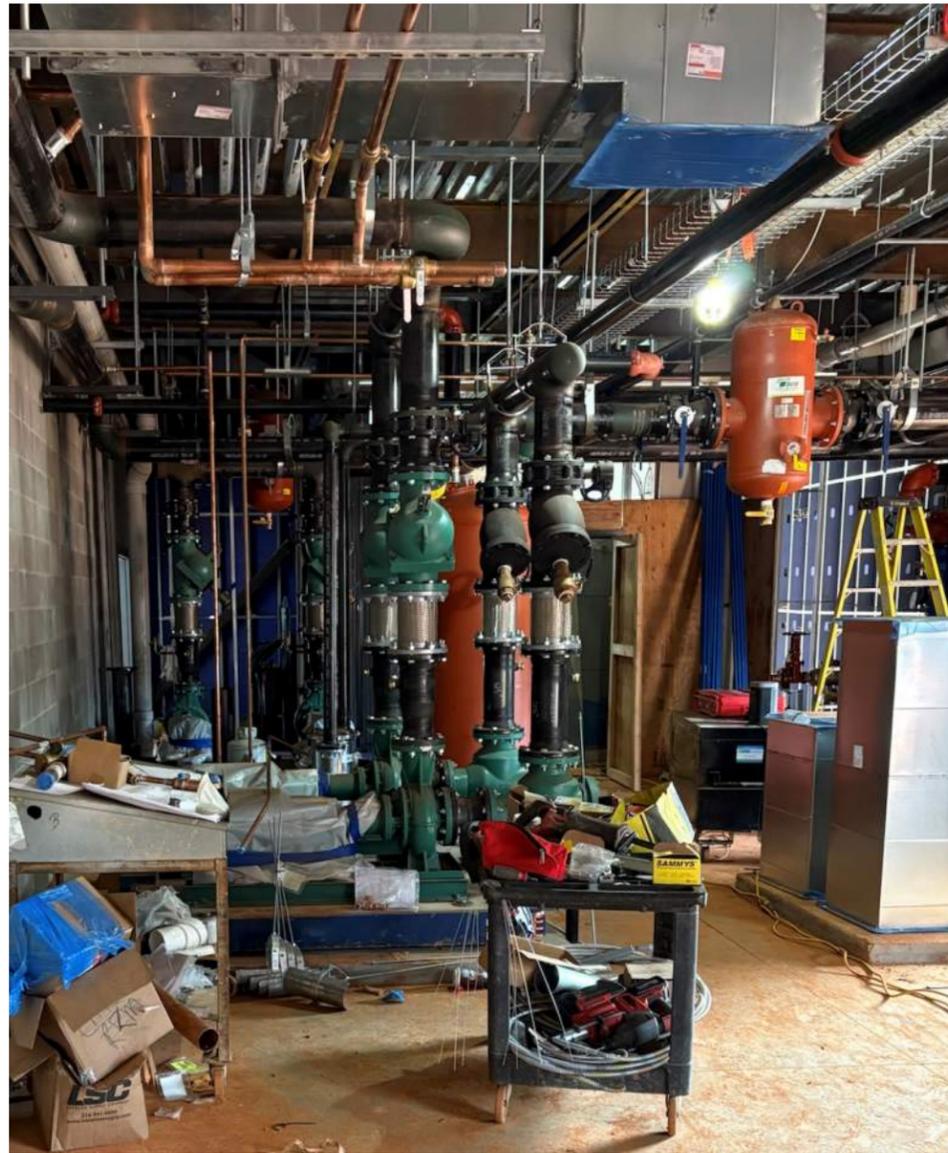

Progress pictures

- Site work – Sidewalk, curb & gutter, asphalt



Open Discussion

For more information, please contact:



Jam Kendrick

pg_jam.kendrick@pgcps.org

pepblueprintschoolsp3.com

