



PGCPS . **ENGAGE . DESIGN . BUILD . COMMUNICATE** . PGCPS



ROBERT FROST K-8 SCHOOL

PROJECT PLANNING COMMITTEE MEETING #4 | MARCH 20, 2025





Agenda

- Design Recap
- Construction Updates
- Open Discussion
- Contact

Design Recap

- No significant design changes since last meeting.
- Building permitting process has begun.
- Demolition / Site Work continues.
- Interior design (Furniture, Finishes and Equipment) is ongoing. Coordination with school needed.
- Writable walls in science is being priced.

Site Plan

- Bus drop-off
- Vehicular parking
- Outdoor classroom and play areas





View of Main Entrance




View of Outdoor Learning



View of Community Entrance - **Previous**



View of Community Entrance - **Current**

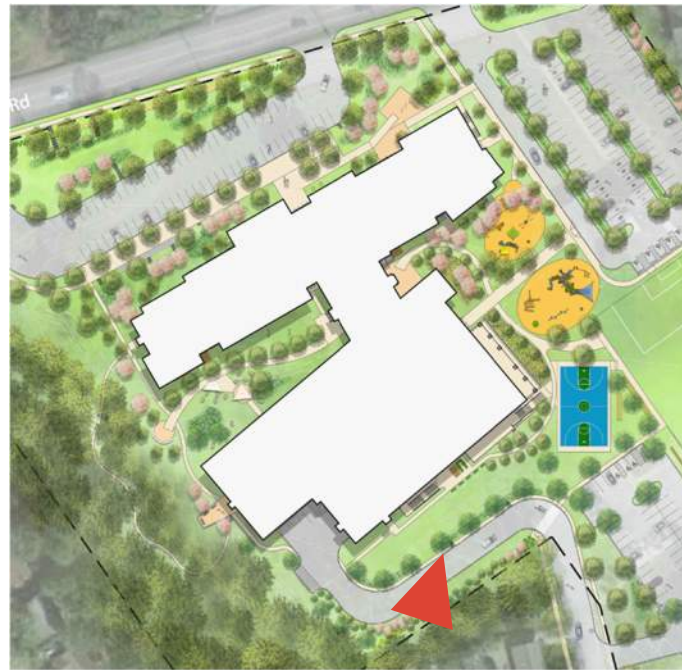

View of Gym Facade

- Early childhood classrooms at grade
- Main entrance
- Heart of the School

DEPARTMENT

	ACADEMIC - CORE
	ACADEMIC - EXTENDED
	ADMINISTRATION
	CIRCULATION
	MEDIA CENTER
	PERF ARTS
	PHYS ED
	SPEC ED
	SUPPORT
	VISUAL ARTS



Note: Design is subject to change



- Elementary and Middle School zones
- Athletics



DEPARTMENT

ACADEMIC - CORE
ACADEMIC - EXTENDED
ADMINISTRATION
CIRCULATION
MEDIA CENTER
PERF ARTS
PHYS ED
SPEC ED
SUPPORT
VISUAL ARTS

Note: Design is subject to change



- Upper grade classrooms
- Elementary and Middle School zones



DEPARTMENT


ACADEMIC - CORE
ACADEMIC - EXTENDED
ADMINISTRATION
CIRCULATION
MEDIA CENTER
PERF ARTS
PHYS ED
SPEC ED
SUPPORT
VISUAL ARTS



Third & Fourth Level Plan

Note: Design is subject to change

Progress Interior Views

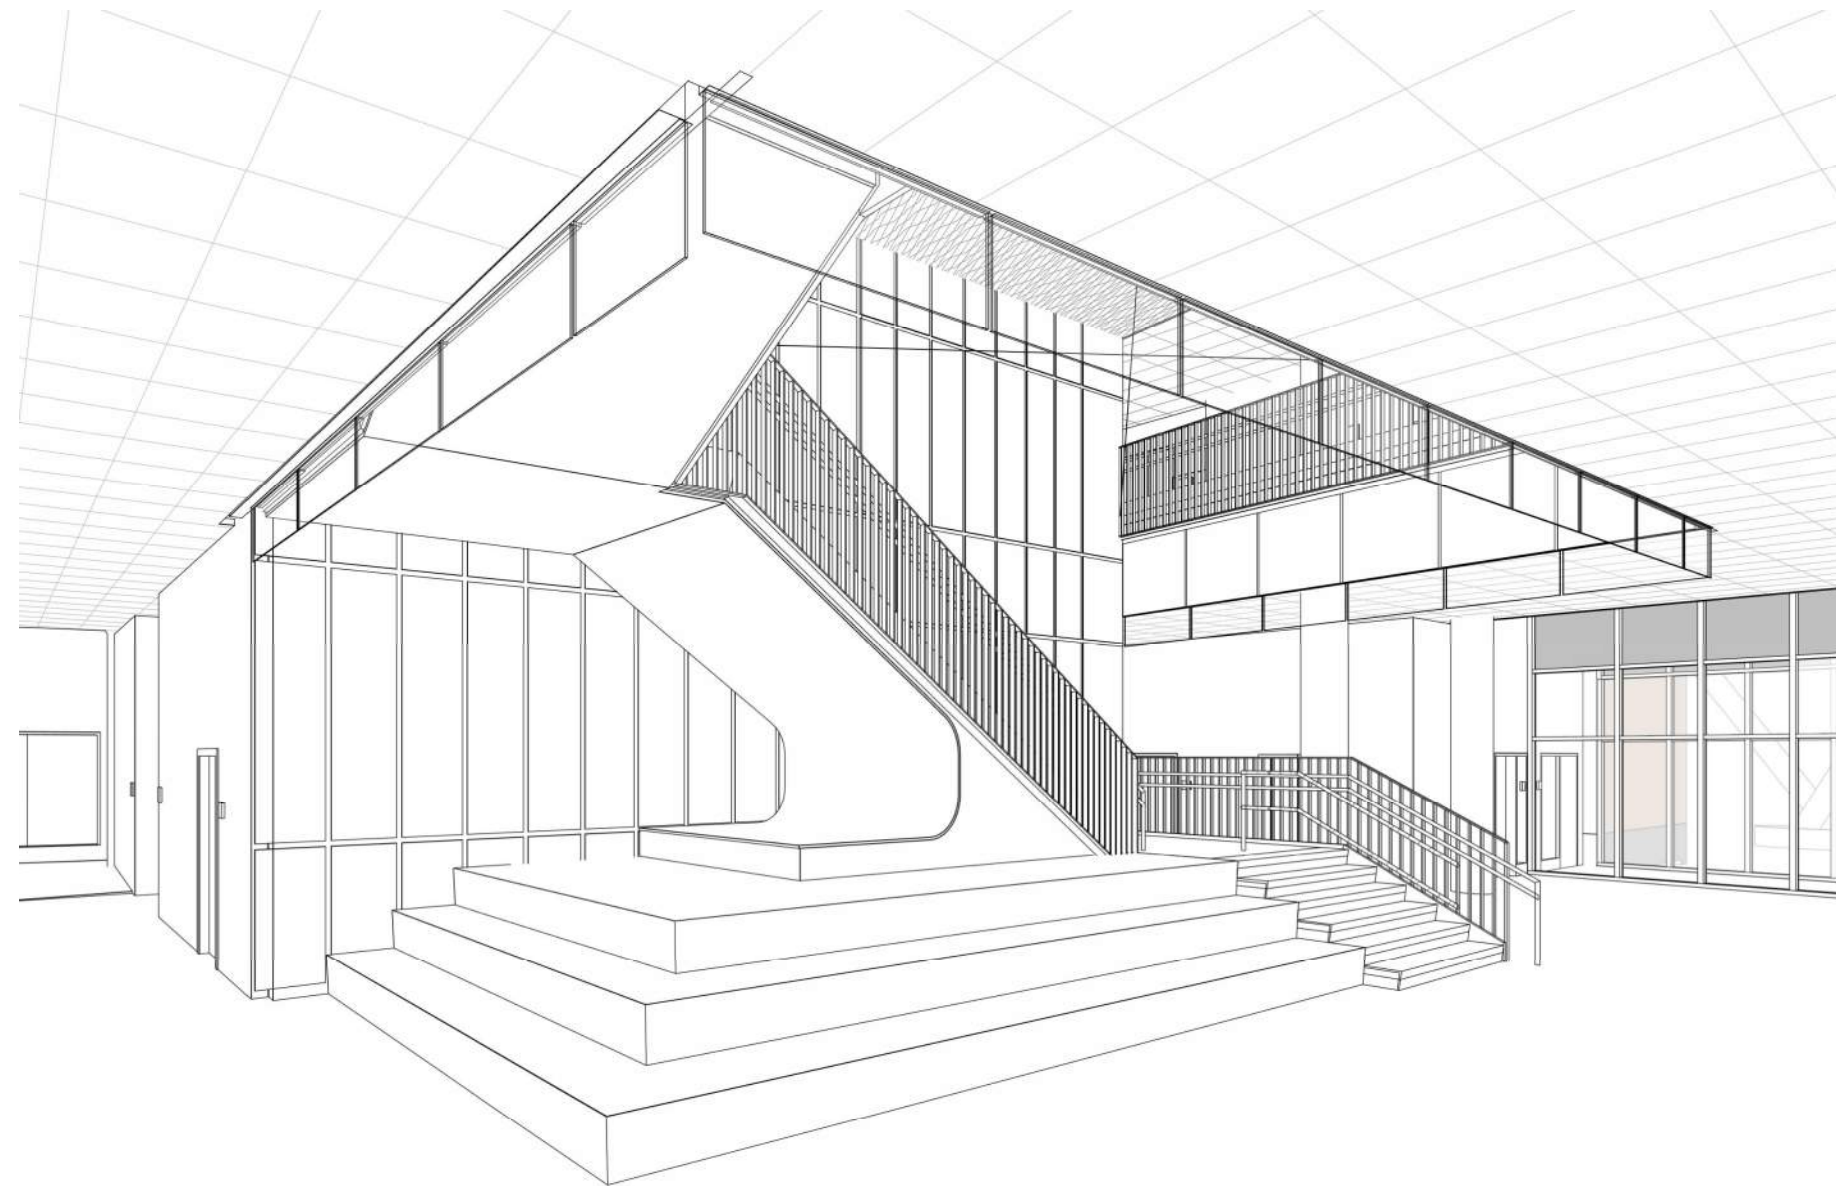

Monumental Stair

- Final finishes to be coordinated with school.


Progress Interior Views



Library

- Final finishes to be coordinated with school.

Schedule Overview

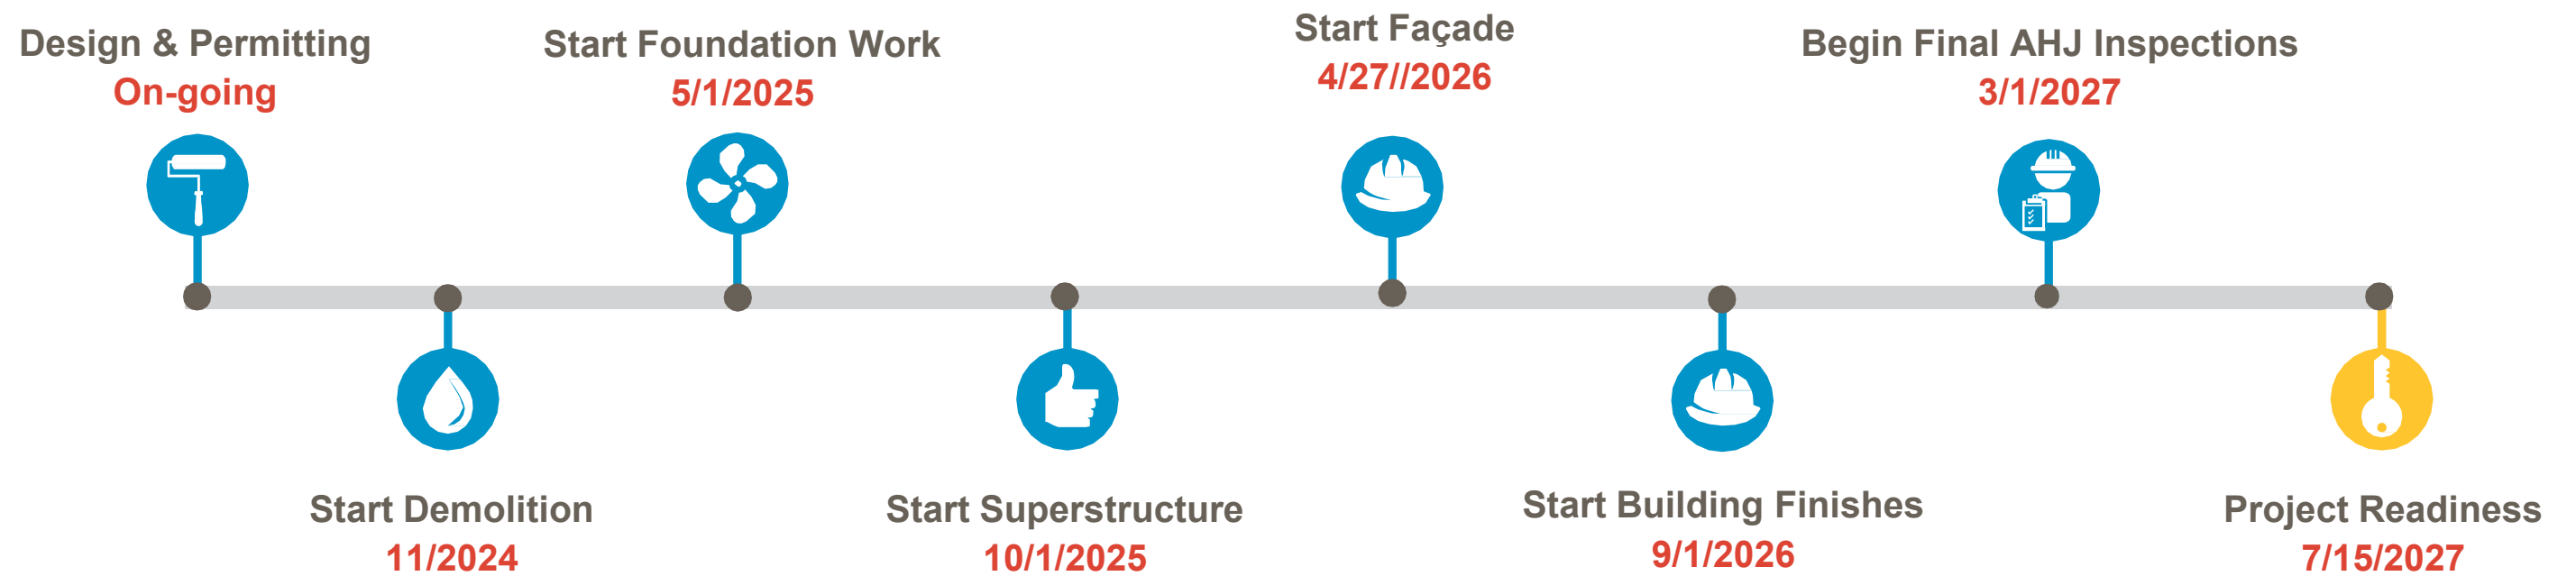

Activities completed

- Establish preliminary Site controls
- Raze of existing building
- Phase 1 Earthwork
- Phase 1 – Tree Conservation Plan
- Set-up Temp power for construction
- Demo Building Foundations
- Phase 2 – Storm Drain structures Installation

Progress Pictures



Progress Pictures



Progress Pictures



Progress Pictures



Upcoming Activities (next 6 weeks)

- Sanitary Relocation onsite
- Geothermal Wells Installation in progress
- Complete Ph-2 Earthwork and Building Pad Grading
- Building Foundations

Open Discussion

For more information, please contact:



Jam Kendrick

pg_jam.kendrick@pgcps.org

pepblueprintschoolsp3.com

